Delivery Metrics-

DORA metric	Meaning for Festivo	How we would measure it	Decision it would trigger
Change lead time	Time from the first code commit for a change until it is available to users. For example, adding the ability to reorder itinerary items on the event dashboard.	Record the first commit timestamp and the production availability timestamp. Include testing, release preparation, and app-store review when required. Calculate average lead time each sprint.	If average change lead time exceeds 7 days in a sprint, we will divide upcoming features into smaller changes and review testing and release blockers twice a week.
Deployment frequency	How often we release changes to Festivo's production environment, such as improvements to vendor search, service requests, or RSVP management.	Count production releases each week. Track mobile app releases and backend deployments separately because they have different release processes.	If no mobile app release occurs over two weeks while completed mobile changes are waiting, we will review release blockers and prepare a smaller release.
Change fail rate	Percentage of production releases that introduce a problem requiring a corrective release, rollback, or feature disablement. Examples include an RSVP update that prevents responses from saving or a vendor-search release that causes crashes.	Divide the number of releases causing failures by total production releases, then multiply by 100. Calculate separately for mobile and backend releases.	If change fail rate exceeds 10% in a sprint, we will require additional regression checks of the affected workflows before the next release.
Rework rate	Percentage of production releases that are unplanned corrections to problems introduced by earlier releases. For example, an emergency update to restore service	Divide unplanned corrective releases by total production releases, then multiply by 100. Count separately for mobile and backend releases.	If rework rate exceeds 20% in a sprint, we will prioritize recurring defects and strengthen regression checks before starting lower-priority features.

	requests after a release breaks submission.		
Recovery time	Time needed to restore affected functionality after detecting a release-related failure. Recovery could involve reverting a backend change, disabling a faulty feature, or distributing a corrected mobile version.	Record the detection timestamp and the timestamp when the affected workflow is verified as working again. For mobile updates, track whether users on the affected version still experience the failure.	If recovery takes more than 4 hours, we will add or improve a recovery option for the affected workflow, such as a backend rollback or remotely controlled feature switch.

Festivo Sketches –




Home page




Itinerary







Vendor search

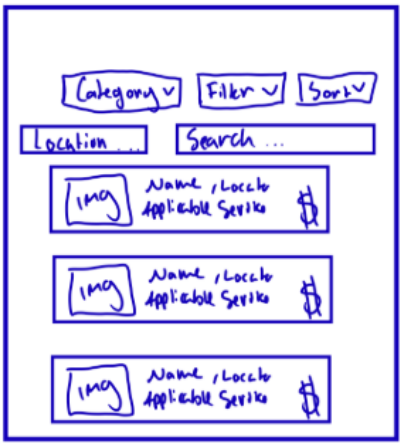


Vendor page

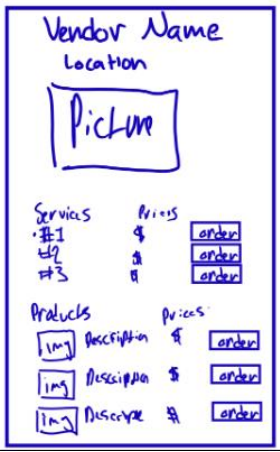


Rsvp


Back
RSVPs
Event Name
Location : Time
Attending
24
Declined
3
Pending
4
Invites
Search Guests . . .
Name 1
of Guests
Name 2
of Guests

Event page


My Events
Edit Event
Event name
Time
Location
RSVP: # Attended
Checklist: Complete
Itinerary
+Add
Edit
Edit
Edit
Choose Vendors/Seats
Name, type, Contact details

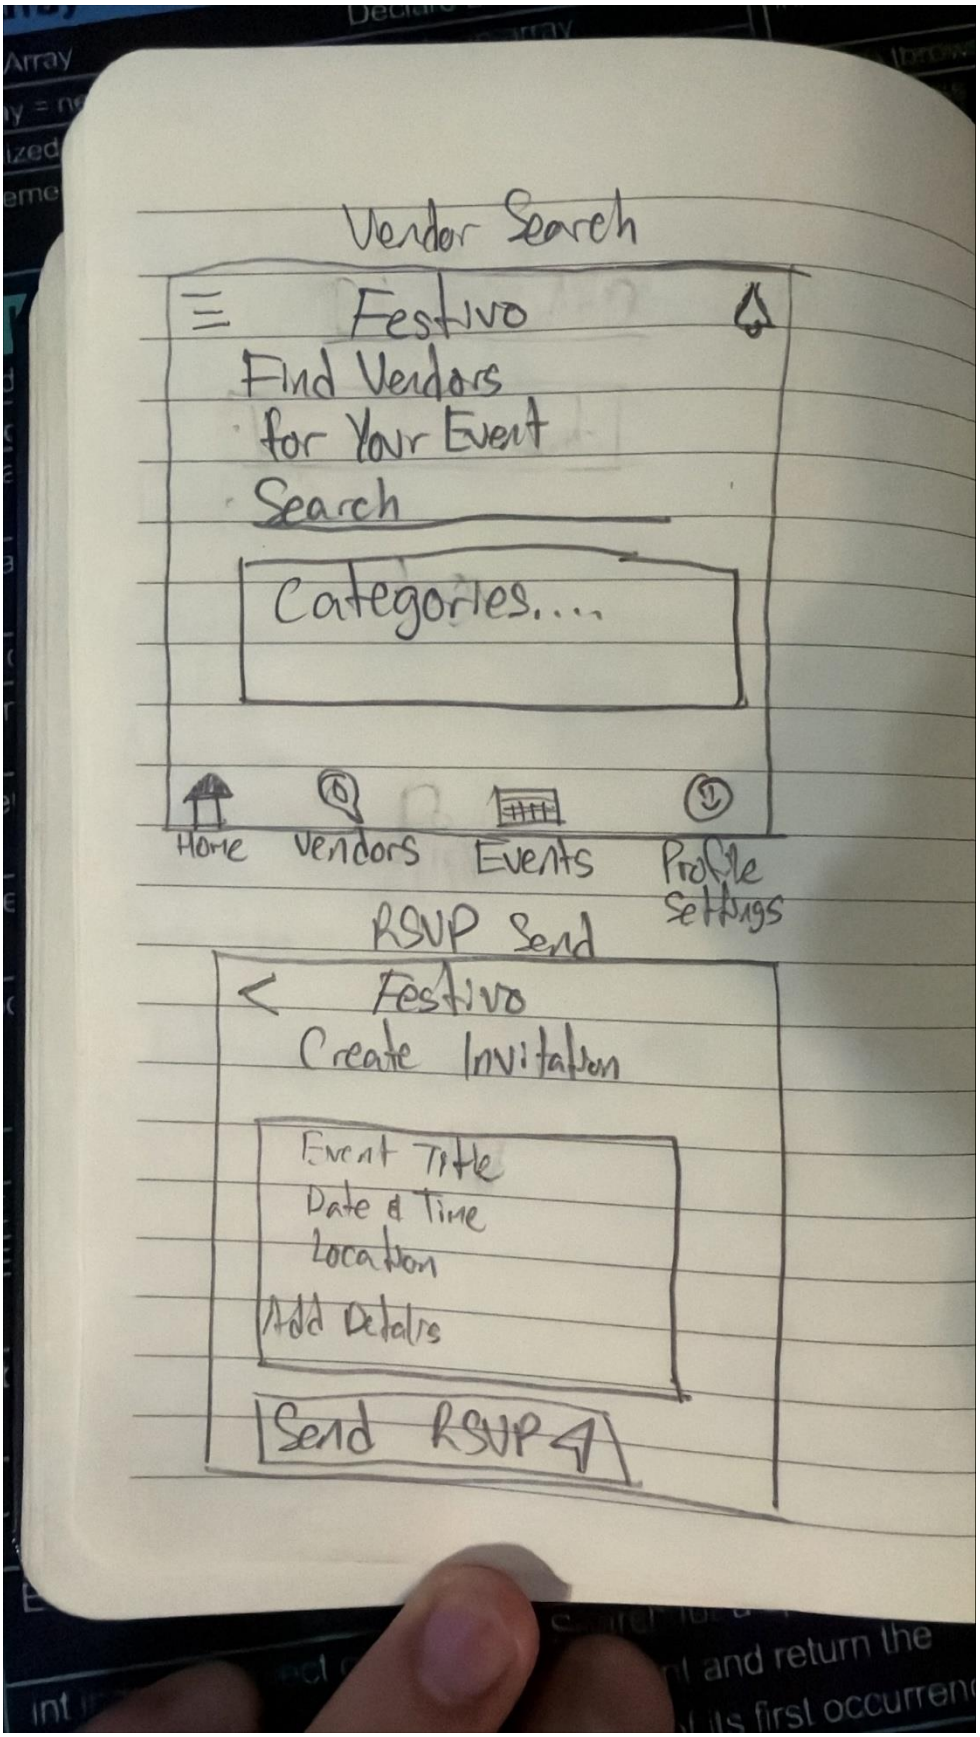
Vendor Search
Festivo
Find Vendors
for Your Event
Search
Categories....
Home
Vendors
Events
Profile
Settings
RSVP Send
Festivo
Create Invitation
Event Title
Date & Time
Location
Add Details
Send RSVP

ect(SocketAddress host eout) throws IOException	Connect the socket server and specify a timeout value
() throws IOException	Close the socket
s getInetAddress()	Return the address of the socket connection
	Return the remote port this

RSVP Receive

< Festivo

Accept Invitation

Grabes BirthDay
Sat, Oct 31, 2026
7:00pm
El Paso Tx

Accept ✓
Maybe ?
Decline X

SLI (Service Level Indicator) - what we measure
Ex.) Percentage of successful vendor searches

SLO (Service level Objective) - our performance target
Ex.) 99% of vendor searches should succeed.


SLA (Service Level Agreement) - a formal service commitment
Festivo commits to a defined availability level, with remedies if it fails.

System.getProperties()


information

excovip

Event page



Home Page



Vending Page

